

New Holiday Park Elementary School Monthly Report



December 5, 2014

Rucon Inc.

WWW.RUCONINC.COM

(PBSD Owners Representative)

“Project is on schedule”


- Gas meter to be set next week
- Grease trap installed and inspected
- Sprinkler piping installation is complete except gym
- Sprinkler head installation ongoing
- Data wire being pulled in cable trays
- Main power transformer has been set
- Roof is dried in for all areas
- Interior block in Kitchen area C ongoing
- Exterior Brick is complete
- Duct work is being built for gym
- Boilers built and tested in mechanical room
- Pipe insulation is ongoing for HVAC & Plumber
- Painting is ongoing in all areas
- Bulk heads ongoing in areas A & C
- Ceiling grid is 95% installed in classrooms
- Drywall installation in admin area to begin this week
- Windows installation in all areas and store fronts in A & B are 95% complete and C & A store fronts will be installed at end of the month
- Driveway and parking lot have had paving binder installed
- Sub surface drain near walking path entrance is ongoing
- Metal panel siding to be delivered in next few weeks

- Inspections are ongoing by Pa Soil & Rock and Plum Borough inspectors and utility companies
- Safety meeting reports have been turned in weekly from contractors

Project Photos



Gas Line

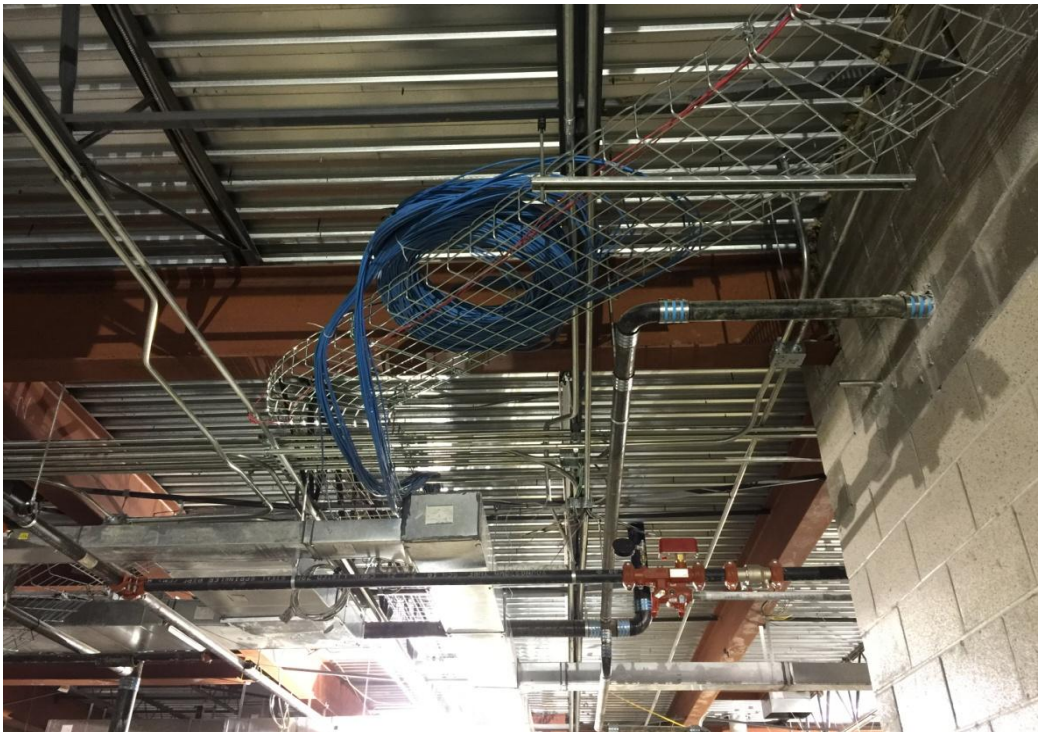

Data wiring



Kitchen area walls



Mechanical room



Duct & Pipe insulation



Bulk heads in library



Parking Lot paved



Driveway paved



Transformer



Grease trap
