

# **New Holiday Park Elementary School Monthly Report**



**January 7, 2015**

**Rucon Inc.**

**WWW.RUCONINC.COM**

**(PBSD Owners Representative)**


# “Project is on schedule”

- Temporary gas meter set for temporary heat
- Sprinkler piping and drops in gym ongoing
- Data wire being installed in all of 2nd floor
- Main power connected to panels
- Roof flashing is complete
- Interior block 98% complete
- Gas lines completed to boilers and water heaters
- Insulation is ongoing for ductwork and piping
- Connections being made in the unit ventilators
- Bulk heads ongoing in areas A & C
- Ceiling grid is 98% installed in classrooms
- Drywall in admin to be finished starting next week
- C & A store fronts will be installed next week
- Metal panel siding and translucent panels to begin installation in next few weeks
- Casework has been delivered for classrooms
- Areas B first floor and B&D 2nd floor casework installed
- Gym floor concrete to be poured next week
- Inspections are ongoing by Pa Soil & Rock and Plum Borough inspectors and utility companies
- Safety meeting reports have been turned in weekly from contractors

## Project Photos



Temporary gas meter

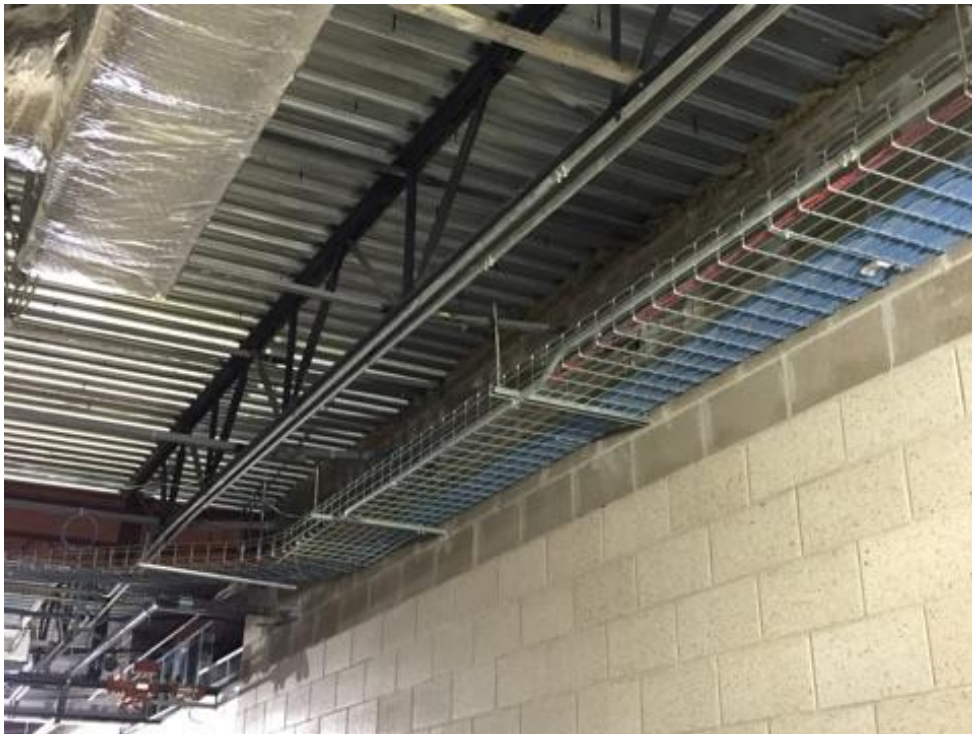

Data wiring on 2nd floor



Corridor walls



Mechanical room gas lines



Bulk heads dry walled



Admin area



Kindergarten casework



Gym floor prepped
